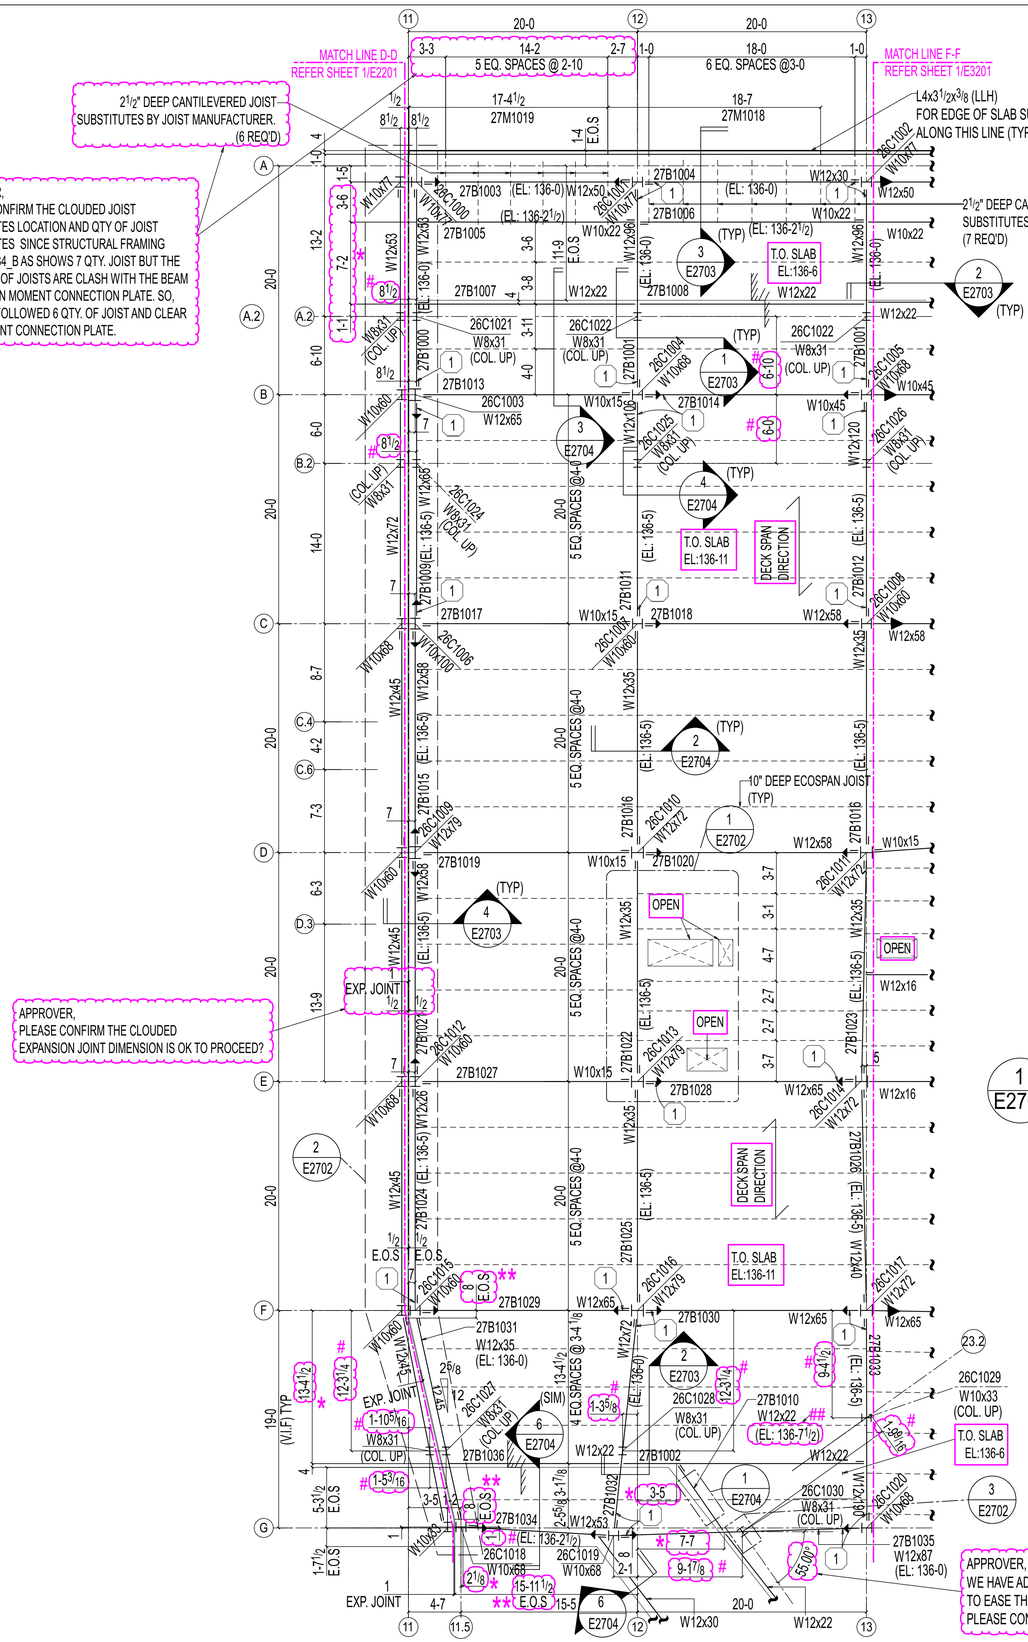

APPROVER,
PLEASE CONFIRM THE CLOUDED JOIST SUBSTITUTES LOCATION AND QTY OF JOIST SUBSTITUTES SINCE STRUCTURAL FRAMING PLAN 1/S134_B AS SHOWS 7 QTY. JOIST BUT THE EACH END OF JOISTS ARE CLASH WITH THE BEAM TO COLUMN MOMENT CONNECTION PLATE. SO, WE HAVE FOLLOWED 6 QTY. OF JOIST AND CLEAR THE MOMENT CONNECTION PLATE.

APPROVER,
PLEASE CONFIRM THE CLOUDED EXPANSION JOINT DIMENSION IS OK TO PROCEED?

★ -APPROVER,
PLEASE CONFIRM THE ALL CLOUDED BEAM LOCATIONS ARE OK TO PROCEED?

★★-APPROVER,
PLEASE CONFIRM THE EDGE OF SLAB DIMENSION IS OK TO PPROCEED?

-APPROVER,
PLEASE CONFIRM THE CLOUDED COLUMN LOCATION IS OK TO PROCEED?

-APPROVER,
PLEASE CONFIRM THE CLOUDED TOP OF BEAM ELEVATION IS OK TO PROCEED? SINCE WE HAVE ADJUSTED THE T.O.S EL. TO MATCH ADJUSCENT BEAM'S TOP.

APPROVER,
PLEASE CONFIRM ALL JOIST SPACINGS ARE OK TO PROCEED?

APPROVER,
THE STRUCTURAL PLAN SHOWS SOME BEAM LOCATIONS OFFSET FROM THE COLUMN CENTER. DUE TO FRAMING CONDITIONS AND CONNECTION REQUIREMENTS, WE HAVE ALIGNED THE BEAMS WITH THE COLUMN CENTER. PLEASE CONFIRM.

APPROVER,
PLEASE CONFIRM IF ANY STEEL IN THIS PROJECT REQUIRES FIRE PROOFING. WE ASSUMED ALL STEEL(LEVEL-09 THRU PENTHOUSE) IN THIS PROJECT WILL BE 1-COAT STANDARD PPG GRAY SHOP PRIMER.

APPROVER,
WE HAVE ADJUSTED THE COLUMN ROTATION TO 55° TO EASE THE BEAM END CONNECTION AT LEVEL- 10. PLEASE CONFIRM.

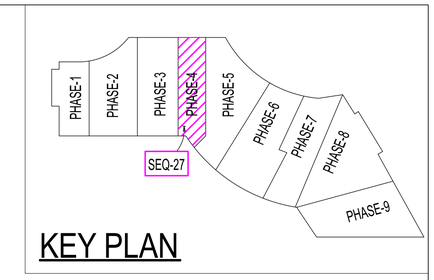

KEY PLAN

1/E2701 PARTIAL LEVEL-09 FRAMING PLAN (PHASE-4)(SEQ#27)

NOTES: (REF: 1/S134_B)

1. TOP OF SLAB EL: 136'-11" (U.N.O).
2. E.O.S - INDICATES EDGE OF SLAB.
3. ▶ - DENOTES MOMENT CONNECTION.
4. ALL FIELD BOLTS SHALL BE ¾" Ø F1852N TC BOLTS.(U.N.O).
5. ALL GRID DIMENSION TO BE VERIFY IN FIELD.(U.N.O).
6. ⟷ - INDICATES METAL DECK SPAN ORIENTATION DIRECTION.
7. ALL ELEVATION SHOWN FOR TOP OF BEAM (U.N.O).
8. - DENOTES SLAB DEVIATION.
9. ALL JOIST TO BE 10" DEEP ECOSPAN COMPOSITE FLOOR JOIST.(U.N.O).
10. TOP OF BEAM EL: 136'-7½".(U.N.O).
11. ALL FIELD BOLTS SHALL BE SNUG TIGHTENED U.N.O
12. ① -DENOTES 1"Ø F2280N TC BOLTS.

APPROVER,
PLEASE REVIEW ALL GRIDS AND GRID SPACINGS AND CONFIRM.

PROJECT NORTH
&
TRUE NORTH

REVISIONS

REV#	DWN BY	DESCRIPTION	DATE
A	MNK	ISSUED FOR APPROVAL	Apr 3 2025

THE INFORMATION NOTED HEREON THIS DRAWING IS THE PROPERTY OF STEEL FAB ENTERPRISES, INC. AND SHALL NOTED BE USED WITHOUT WRITTEN CONSENT.

STEEL FAB ENTERPRISES, LLC
AISC CERTIFIED FABRICATOR AND ERECTOR
MISCELLANEOUS METALS FABRICATOR AND ERECTORS
623 BAUMGARDNER ROAD, LANCASTER, PA 17603
TEL. (717)464-0330 FAX (717)464-9464
WWW.STEELFABENTERPRISES.COM

PROJECT OWNER : HP NAREF, 1250 MARYLAND HOLDINGS 1 LP.
PROJECT DESCRIPTION : 1250 MARYLAND AVENUE
PROJECT ADDRESS : 1250 MARYLAND AVENUE, WASHINGTON, DC 20024
CONTRACTOR : IRON FABRICATION SERVICES, INC.

DRAWN BY : JSV	DATE : 02-27-2025	PROJ. NO. : 25001	REV # A
CHECKED BY : MNK	DATE : 02-27-2025	DWG NO. : E2701	

DWG DESCRIPTION : PARTIAL LEVEL-09 FRAMING PLAN (PHASE-4) (SEQ#27)
